

Berkeley Heights Municipal Complex

Construction Forecast

September 3, 2018 – September 16, 2018

Activity	Affected Areas	Noise	Dust	Vibration	Odor	9/3	9/4	9/5	9/6	9/7	9/8	9/9	9/10	9/11	9/12	9/13	9/14	9/15	9/16	
						Mon	Tues	Wed	Thur	Fri	Sat	Sun	Mon	Tues	Wed	Thur	Fri	Sat	Sun	
Site Layout	New Salt Dome									X										
Finalize Trailer Electric Installation	New Salt Dome/Trailer Location						X	X	X	X										
Excavating Undercuts Around Salt Dome	New Salt Dome Area						X	X	X											
Excavate Material From Building Area & Backfill	New Building Area & New Salt Dome Area						X	X	X	X										
Install Utilities at Salt Dome	New Salt Dome Area												X	X	X					
Paving at Salt Dome	New Salt Dome Area														X	X				
Process Submittals	N/A						X	X	X	X			X	X	X	X	X	X		
Epic Subcontractor Procurement	N/A						X	X	X	X			X	X	X	X	X	X		

LEGEND ■ High ■ Moderate ■ Low

Note: Schedule is subject to change


PHOTOS FROM THE PREVIOUS WEEK:



Backfilling at the New Salt Dome



Stone for the base of the New Salt Dome

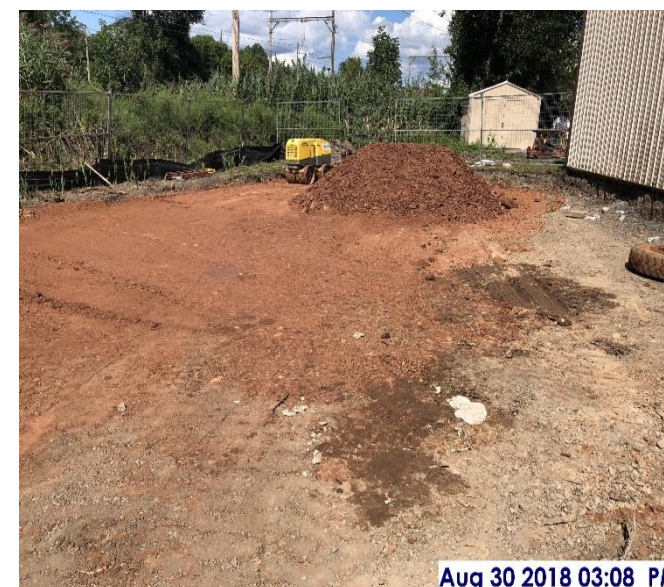

Compaction operations adjacent to New Salt Dome



New electrical service panels at site trailers
